



Ad Hoc Stormwater Utility and Flood Mitigation Advisory Group

November 8, 2023 Meeting



Tonight's Agenda

- 1. Approve previous meeting minutes (6:00 pm, 5min)
- 2. Project update by City staff (6:05pm, 15min)
- 3. Outreach update by group members (6:20pm, 15min)
- 4. Letter of support for FY2025 SW Fee (6:35pm, 10min)
- 5. Letter of support for application to Community Flood Preparedness Fund (6:45pm, 10 min)
- 6. Follow-on discussion of flow sensors (6:50pm, 20min)
- 7. Preparation for Annual Report on the FY2025 Stormwater Budget (7:10pm, 15min)
- 8. Proposed schedule of meetings from now until July 2024 (7:25pm, 10min)
- 9. Public Comment (7:35pm, 5 min)
- 10. Adjourn (7:40 pm)



Approval of Minutes from Last Meeting



Update on Flood Action Alexandria Program



Flood Action Progress Report: Large Capacity Projects & CSS

- Large capacity projects
 - Commonwealth/Ashby/Glebe (est. \$50M) 30% submission received on 9/21, City coordinating comments. Design development towards 60%. Continued coordination with utilities for relocation. Development of geotechnical report based on site borings underway.
 - Hooffs Run Culvert Bypass (est. \$60M) Fieldwork component of field survey along Russell Road is complete. An existing model of the culverts and overland flooding has been developed. The team is exploring potential alternatives according to multiple metrics that account for flood mitigation effectiveness, complexity, cost, and impact. The on-going community questionnaire will close Dec 8th, 2023.
- Combined sewer system (CSS) area projects
 - Pitt & Gibbon (\$20-25M) Planning Phase Site meeting to finalize survey limits. Surveyors developed proposal based on final survey limits. Mobilization expected mid-November.
 - Nethergate (\$5M) Planning Phase Field survey complete end of last month. After delivery of survey, design team will finalize alternative. Move to design/NPS permit process



Flood Action Progress Report: Updates to Stormwater Program Schedule

Project Schedule Extended

- •CFM Storm Sewer Improvements (Design Procurement)
- •Edison St. Cul-de-Sac Drainage Improvements (Design)
- •Mt. Vernon Cul-de-sac Inlets & Alley (Construction Procurement)
- •F. Hammond Culvert Headwall Modifications (Construction Procurement)
- •Hume Ave Stormdrain Bypass (Design)
- •Lloyd's Lane (Construction Procurement)
- •N. Overlook Drainage (Construction Procurement)
- •W. Reed Ave. Curb Inlets & Dale Street Drainage Improvements (Design)

Project Delivery Expedited

- 100 Hume Ave SD Bypass (ARPA* Funding Secured)
- Edison St. Drainage Improvement (CFPF* Funding Secured)
- 100 W. Reed Curb Inlets (CFPF Funding Secured)
- 100 Dale Rd. Overland Relief Channel (CFPF Funding Secured)
- Mt. Vernon and Edison Dual CMP Replacement (CFPF Funding Secured)
- 00 E. Linden Ave. Alleyway Improvements
- CFM Green Alley (HUD* Funding secured)

ARPA* – American Rescue Plan Act CFPF* – Community Flood Preparedness Fund HUD* – Housing and Urban Development



Flood Action Progress Report: Updates to Stormwater Program Schedule

Milestones

- 100 Hume Ave Stormdrain Bypass (90% Design NTP)
- W. Reed Ave. Curb Inlets & Dale Street Drainage Improvements (90% NTP)
- Edison St. Cul-de-Sac Drainage Improvements (90% NTP)
- N. Overlook Drainage (Awarded to Sagres Construction)
- Mt. Vernon Cul-de-Sac and Alley (Construction Procurement Begins)

Start Date contingent on Hoofs Run Culvert Bypass

- 300 E. Mason Curb Inlets
- E. Monroe Ave. & Newton St. Curb Inlet
- E. Alexandria Ave. & E. Luray Ave Curb Inlets
- 500 E. Alexandria Ave. Alleyway Stormdrain Extension
- 300 E. Mason Ave. Stormdrain Extension
- 300 E. Mason Ave. & 200 E. Duncan Ave Stormdrain Connection



Maintenance Activities

- Hooffs Run Channel Maintenance completed:
 - Inlet cleaning between Linden and Rosemont Streets completed.
- Hooffs Run Culvert Inspection
 - Pre and post storm inlet inspections and cleaning
 - Coordinating inspection schedule with vendor: November- December 2023
 - Cleaning will be based on the inspection findings
 - Proposing to inspect yearly

Sanitary Sewer Asset Renewal Program: Del Ray East Rehabilitation Project

OF ALEXANDER OF A STATE OF A STAT

Summary of Work

- 150 pipe segments to be rehabilitated using ultraviolet (UV) cured-in-place pipe (CIPP) technology
- 111 manholes to be rehabilitated

Contractor Notice to Proceed Issued October 16th

- Work to generally start from south and move to the north
- Residents will be provided with 2-week and 48hour notification if the sewer main serving their home is to be rehabilitated
- No parking signs to be posted 72 hours in advance of work





Outreach Update



Communications

- 132 total messages were received from all social media channels with 35 of them originating from Facebook, an increase of 12.9%.
- Impressions decreased by 7.7%. (46,705)
- Engagement decreased by 3.3%. (1,445)
- Post link clicks decreased by 24.4%. (133)
- Popular content included King Street projects, (Traffic and Stormwater Management related) Pedestrian Safety Month, and recycling.



Letter of support for FY2025 SW Fee



Letter of support for application to Community Flood Preparedness Fund AGENDA ITEM #5



Follow-on discussion of flow sensors




Annual Report on the FY2025 Stormwater Budget AGENDA ITEM #7

Annual Report Discussion – The right places? Adequate funding? Sufficient progress?

Urgent big projects getting started & spot improvements getting done

September 10, 2020 Rain Event

Heat Map Showing Flood-related Requests for Service

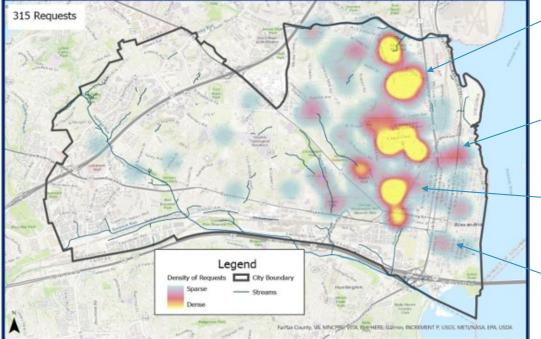

Large Capacity Projects:

Commonwealth, Ashby, Glebe

Design started: 7/2022 Construction starts: 4/2026 Cost: \$50M

Nethergate

Design starts: 1/2024
Construction starts: 7/2025
Cost: \$5M

Hooff's Run

Design started: 5/2023 Construction starts: 9/2026 Cost: \$60M

Pitt & Gibbon


Design starts: 12/2023 Construction starts: 9/2027 Cost: \$12M





Annual Report Discussion – The right places? Adequate funding? Sufficient progress?

Construction is still years away & more projects beyond...so don't let up!

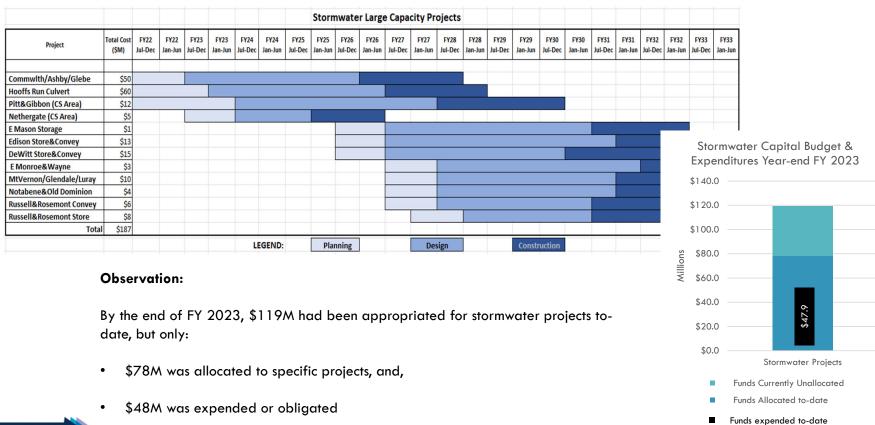







Proposed schedule of future meetings



Public Comment



Adjourn
